

PROGRESS UPDATE REPORT NO. 2

Project: Brighton Wastewater Treatment System Upgrades
Client: The Municipality of Brighton Contractor: North America Construction (1993) Ltd.

With the exception of the items noted, the work appears to be proceeding in general accordance with the requirements and intent of the design documents.

Date: From February 5, 2026 To March 6, 2026

1.0 PROJECT STATUS

1.1 Schedule

- A baseline schedule has not been approved to date. NAC's weekly planning aid submissions have been used for scheduling purposes.

1.2 Budget

- Project is currently on budget.

Contract Amount	\$50,122,781.02
Work Completed and Material Supplied to Date	\$2,150,275.83
Remaining	\$47,972,505.19
- NAC is still working on breaking down some items in their schedule of values and in the interim are not billing against them.

1.3 Environment

- No environmental issues raised during this period.

1.4 Health & Safety

- February 5th, 2026, one worker bumped knee on skid steer. No medical aid was required and ice was applied. No time loss from incident.

2.0 PROGRESS OF WORK

2.1 Municipal Fill Site

- Site prep (NAC)
- Receive fill (NAC)

2.2 Siteworks

- Office trailer setup (NAC)
- Hydro pole line installation (PBW)
- Distribution can wiring (NAC)
- WWTP road prep (AWD)
- Power to office trailer complex (NAC)
- Haul topsoil offsite (AWD)
- Pumping station overburden excavation (AWD)
- Pumping station rock excavation (AWD)
- Hydro one connection (PBW/Hydro)

3.0 UPCOMING WORK

PROGRESS UPDATE REPORT NO. 2

3.1 Siteworks

- Bulk excavation (AWD) [March 9-22]
- WWTP road prep (AWD) [March 9-10]

3.2 Yard Piping

- Planning of work dependant on confirmation of delivery of structures

3.3 Concrete Works

- Mudslab at sewage pump station (SPS) (NAC) [March 17]
- Baseslab FRP at SPS (NAC) [March 18-26]
- Walls FRP at SPS (NAC) [March 27-]
- HDPE liner install (NAC) [April 7-]

PROGRESS UPDATE REPORT NO. 2 - PHOTOS



Photo 1: March 2



Photo 2: March 2

PROGRESS UPDATE REPORT NO. 2 - PHOTOS



Photo 3: March 2



Photo 4: March 2

PROGRESS UPDATE REPORT NO. 2 - PHOTOS



Photo 5: March 2 (pit)



Photo 6: March 2 (pit)

PROGRESS UPDATE REPORT NO. 2 - PHOTOS



Photo 7: March 3 (pumping station)



Photo 8: March 3

PROGRESS UPDATE REPORT NO. 2 - PHOTOS

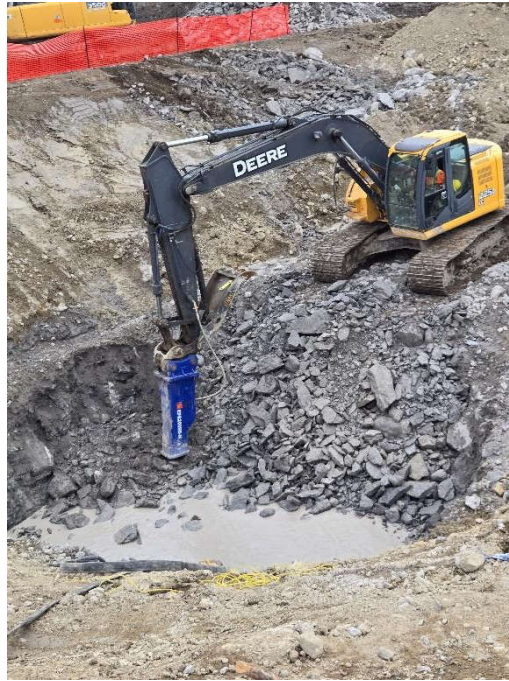


Photo 9: March 6 (pumping station)



Photo 10: March 6 (pumping station)

PROGRESS UPDATE REPORT NO. 2 - PHOTOS

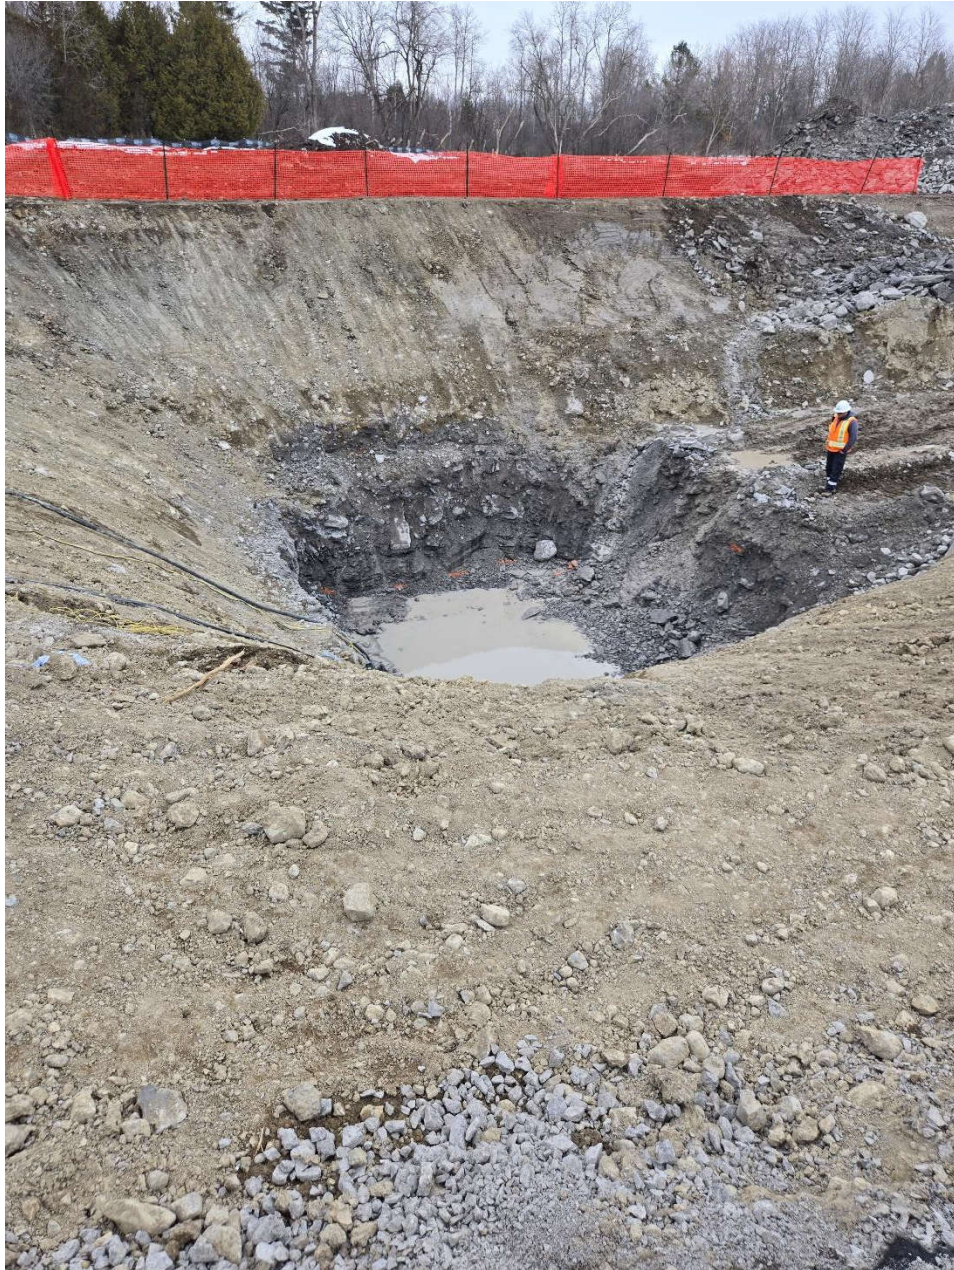


Photo 31: March 6 (pumping station)
