

PROGRESS UPDATE REPORT NO. 1

Project: Brighton Wastewater Treatment System Upgrades
Client: The Municipality of Brighton Contractor: North America Construction (1993) Ltd.

With the exception of the items noted, the work appears to be proceeding in general accordance with the requirements and intent of the design documents.

Date: From Mobilization To February 5, 2026

1.0 PROJECT STATUS

1.1 Schedule

- The ready-for-takeover date was pushed back from September 26th, 2027, to October 15th, 2027, due to contract signing delay.
- A baseline schedule has not been approved to date. NAC's weekly planning aid submissions have been used for scheduling purposes.

1.2 Budget

- Project is currently on budget.

Contract Amount	\$50,122,781.02
Work Completed and Material Supplied to Date	\$2,150,275.83
Remaining	\$47,972,505.19
- NAC is still working on breaking down some items in their schedule of values and in the interim are not billing against them.

1.3 Environment

- While stripping topsoil, NAC's earthworks sub encountered isolated pockets of buried garbage within the excavation footprint. Following Cambium's review, NAC was instructed to dispose of the garbage at Northumberland County Landfill as solid non-hazardous waste. On January 14th, after all garbage has been excavated, NAC's sub backfilled and compacted the void left with native material.
- Soil discolouration below drying bed was observed and Cambium addressed it. Their report stated that as long as this soil is re-used on site then there is no issue.

1.4 Health & Safety

- No safety incidents reported.

2.0 PROGRESS OF WORK

2.1 Siteworks

- Erosion controls (AWD)
- Clearing and grubbing (AWD)
- Demo of dry bed (AWD)
- Stripping topsoil (AWD)
- Perimeter fencing install (NAC)
- Vibration and settlement monitoring baseline readings (Englobe)
- Well decommissioning (Insitu)
- Creek water sampling (Insitu)

PROGRESS UPDATE REPORT NO. 1

- MH 131 investigation (NAC)
- Cut fill northside of site (AWD)
- Office Trailer Setup (NAC)
- Municipal Pit Prep (AWD)

3.0 UPCOMING WORK

3.1 Siteworks

- WWTP Road Prep (AWD)
- Haul Topsoil Offsite (AWD)
- Pumping Station Overburden Excavation (AWD)
- Pumping Station Rock Excavation (AWD)

3.2 Yard Piping

- MH11 Install (AWD)
- 600 mm Pipe Install MH11-MH10 (AWD)
- Install MH10 (AWD)
- 600 mm Pipe Install MH10-MH09 (AWD)
- Install MH09 (AWD)

PROGRESS UPDATE REPORT NO. 1 - PHOTOS



Photo 1: 2026-02-04

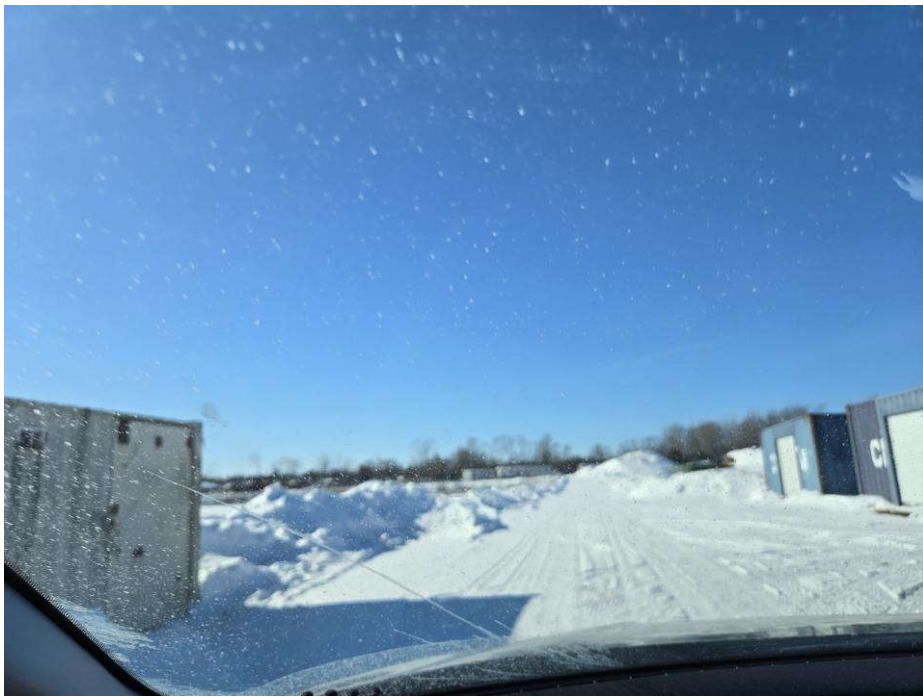


Photo 2: 2026-02-04

PROGRESS UPDATE REPORT NO. 1 - PHOTOS



Photo 3: 2026-02-04



Photo 4: 2026-02-04

PROGRESS UPDATE REPORT NO. 1 - PHOTOS



Photo 5: 2026-02-04



Photo 6: 2026-02-04

PROGRESS UPDATE REPORT NO. 1 - PHOTOS



Photo 7: 2026-02-04



Photo 8: 2026-02-04

PROGRESS UPDATE REPORT NO. 1 - PHOTOS



Photo 9: 2026-02-04



Photo 10: 2026-02-04

PROGRESS UPDATE REPORT NO. 1 - PHOTOS



Photo 31: 2026-02-04



Photo 14: 2026-02-04

PROGRESS UPDATE REPORT NO. 1 - PHOTOS

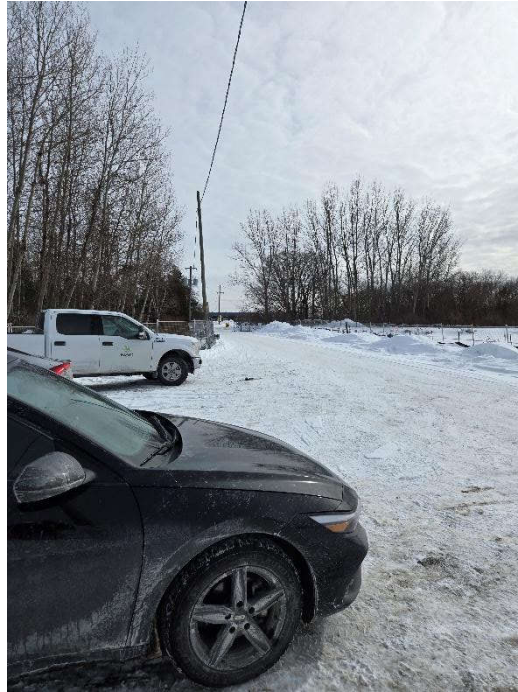


Photo 53: 2026-02-05



Photo 14: 2026-02-05

PROGRESS UPDATE REPORT NO. 1 - PHOTOS



Photo 65: 2026-02-05



Photo 16: 2026-02-05

PROGRESS UPDATE REPORT NO. 1 - PHOTOS



Photo 77: 2026-02-05



Photo 18: 2026-02-05

PROGRESS UPDATE REPORT NO. 1 - PHOTOS



Photo 89: 2026-02-05



Photo 20: 2026-02-05

PROGRESS UPDATE REPORT NO. 1 - PHOTOS



Photo 21: 2026-02-05

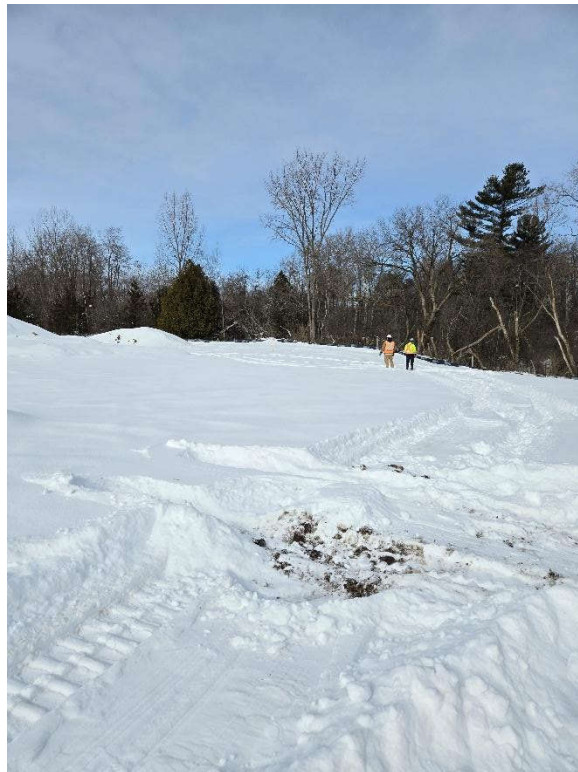


Photo 22: 2026-02-05
