

PROGRESS UPDATE REPORT NO. 8

Project: Brighton Wastewater Treatment System Upgrades
Client: The Municipality of Brighton Contractor: North America Construction (1993) Ltd.

With the exception of the items noted, the work appears to be proceeding in general accordance with the requirements and intent of the design documents.

Date: From August 7, 2026 To September 2, 2026

1.0 **PROJECT STATUS**

1.1 **Schedule**

- Weekly planning aids submitted by NAC and the approved baseline schedule are reviewed and used for scheduling purposes.

1.2 **Budget**

- Project is currently on budget.

Contract Amount	\$50,122,781.00
Work Completed and Material Supplied to Date	\$12,925,103.76
Remaining	\$37,197,677.24

1.3 **Environment**

- Arena Creek monitoring is ongoing with no issues reported.
- A beaver damn north of site is continuing to be monitored.

1.4 **Health & Safety**

- No health and safety issues noted during this period.

2.0 **PROGRESS OF WORK**

2.1 **Municipal Fill Site**

- Receive fill
- Clean up

2.2 **Bypass Pumping**

- Wash piping
- Demob equipment

2.3 **Yard Piping**

- Watermain
- Outfall piping
- Sanitary piping

2.4 **Pump Station**

- Earthworks
- Concrete works
- Mechanical works

PROGRESS UPDATE REPORT NO. 8

2.5 Headworks

- Earthworks
- Concrete works

2.6 Aeration

- Earthworks
- Concrete works

2.7 Clarifier

- Earthworks
- Concrete works

2.8 UV Building

- Concrete works

2.9 Process Building

- Earthworks
- Concrete works
- Mechanical works

2.10 Admin Building

- Earthworks
- Building construction
- Concrete works
- Mechanical works

3.0 UPCOMING WORK

3.1 By-pass Pumping

- Wash piping
- Demob equipment

3.2 Headworks

- Concrete Works

3.3 Aeration

- Concrete works

3.4 Clarifier

- Concrete Works

3.5 UV Building

- Concrete Works

3.6 Admin Building

- Concrete works
- Mechanical works

PROGRESS UPDATE REPORT NO. 8 - PHOTOS



Photo 1: August 7 (aeration and clarifier tanks)



Photo 2: August 13 (aeration and clarifier tanks)

PROGRESS UPDATE REPORT NO. 8 - PHOTOS



Photo 3: August 17 (admin building)



Photo 4: August 18 (tank slab)

PROGRESS UPDATE REPORT NO. 8 - PHOTOS

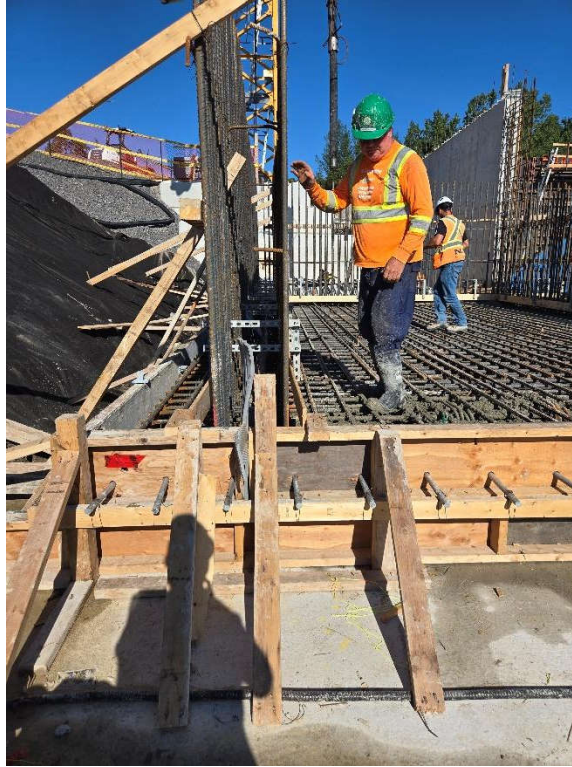


Photo 5: August 18 (tank slab)



Photo 6: August 21 (clarifier and aeration tanks)

PROGRESS UPDATE REPORT NO. 8 - PHOTOS



Photo 7: August 24 (aeration tank wall)



Photo 8: August 25 (facultative lagoon)

PROGRESS UPDATE REPORT NO. 8 - PHOTOS

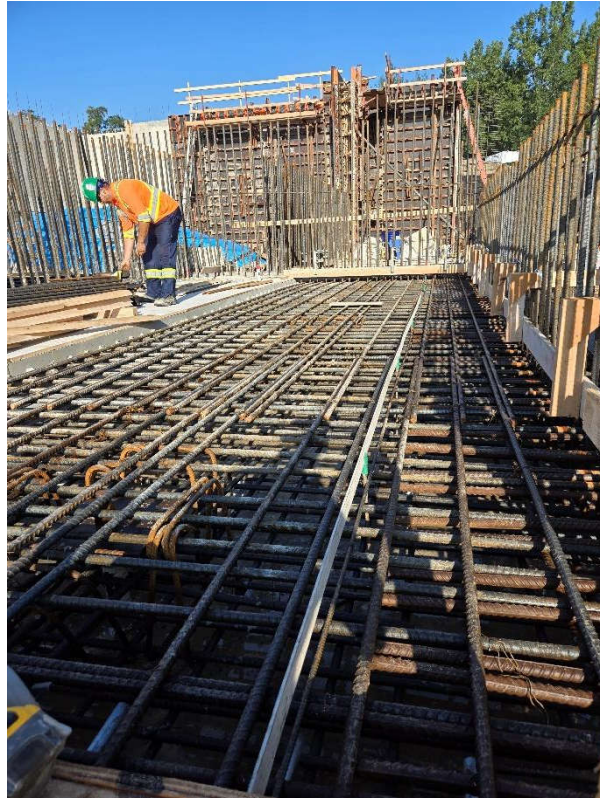


Photo 9: August 26 (tank rebar)



Photo 10: August 27 (aerated lagoon)

PROGRESS UPDATE REPORT NO. 8 - PHOTOS



Photo 11: August 27 (pipe)



Photo 12: August 28 (rock anchor installation for clarifier tanks)

PROGRESS UPDATE REPORT NO. 8 - PHOTOS

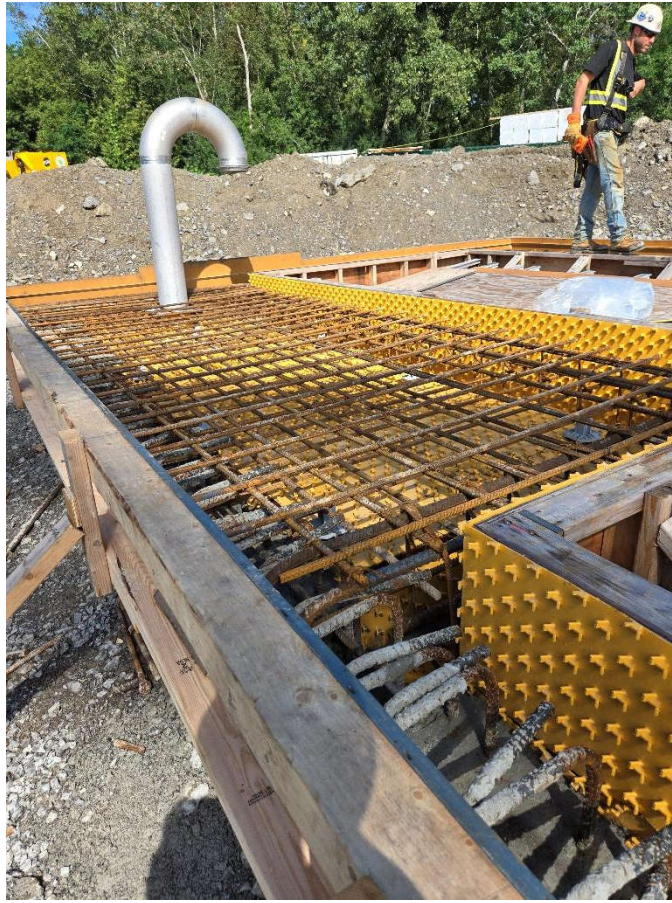


Photo 13: September 2 (pumping station)



Photo 14: September 2 (clarifier/aeration tanks and headworks/UV building)
