J.L.Richards
ENGINEERS · ARCHITECTS · PLANNERS

J.L. Richards
& Associates Limited
203-863 Princess Street
Kingston, ON Canada
K7L 5N4
Tel: 613 544 1424
Fax: 613 728 6012

PROGRESS UPDATE REPORT NO. 9

Project: Brighton Wastewater Treatment System Upgrades

Client: The Municipality of Brighton

Contractor: North America Construction (1993) Ltd.

With the exception of the items noted, the work appears to be proceeding in general accordance with the requirements and intent of the design documents.

Date: From September 3, 2026 To October 1, 2026

1.0 PROJECT STATUS

1.1 Schedule

- Weekly planning aids submitted by NAC and the approved baseline schedule are reviewed and used for scheduling purposes.

1.2 Budget

- The project is currently on budget.

Contract Amount	$50,122,781.00
Work Completed and Material Supplied to Date	$15,351,101.25
Remaining	$34,771,679.75

1.3 Environment

- Arena Creek monitoring is ongoing with no issues reported.
- No beaver activity has been reported.

1.4 Health & Safety

- One worked rolled their ankle but are doing fine.
- One worker was sent to the hospital after mishandling an angle grinder. This individual was warned multiple times how they were using it was unsafe. They are doing fine.
- The contractor properly handled both incidents and filled out the necessary paperwork.

2.0 PROGRESS OF WORK

2.1 Municipal Fill Site

- Tidy

2.2 Yard Piping

- Watermain
- Outfall piping
- Sanitary piping

2.3 Yard Electrical

- Excavation

2.4 Pump Station

- Earthworks
- Concrete works

J.L.Richards
ENGINEERS · ARCHITECTS · PLANNERS

J.L. Richards
& Associates Limited
203-863 Princess Street
Kingston, ON Canada
K7L 5N4
Tel: 613 544 1424
Fax: 613 728 6012

PROGRESS UPDATE REPORT NO. 9

2.5 Headworks
- Earthworks
- Concrete works

2.6 Aeration
- Earthworks
- Concrete works

2.7 Clarifier
- Earthworks
- Concrete works

2.8 UV Building
- Concrete works

2.9 Process Building
- Concrete works

2.10 Admin Building
- Building construction
- Concrete works
- Mechanical works

3.0 UPCOMING WORK

3.1 Municipal Fill Site
- Hydroseed

3.2 Yard Piping
- Outfall piping

3.3 Headworks
- Concrete Works

3.4 Aeration
- Concrete works

3.5 Clarifier
- Concrete Works

3.6 UV Building
- Concrete works

3.7 Admin Building
- Building construction

PROGRESS UPDATE REPORT NO. 9 - PHOTOS



Photo 1: September 8 (aeration and clarifier tanks)



Photo 2: September 8 (manholes and pipe)

PROGRESS UPDATE REPORT NO. 9 - PHOTOS



Photo 3: September 9 (headworks building)



Photo 4: September 10 (admin building)

PROGRESS UPDATE REPORT NO. 9 - PHOTOS



Photo 5: September 17 (hopper rebar)



Photo 6: September 17 (watermain installation)

PROGRESS UPDATE REPORT NO. 9 - PHOTOS



Photo 7: September 17 (hoppers and process building)



Photo 8: September 18 (facultative lagoon)

PROGRESS UPDATE REPORT NO. 9 - PHOTOS



Photo 9: September 21 (admin building)

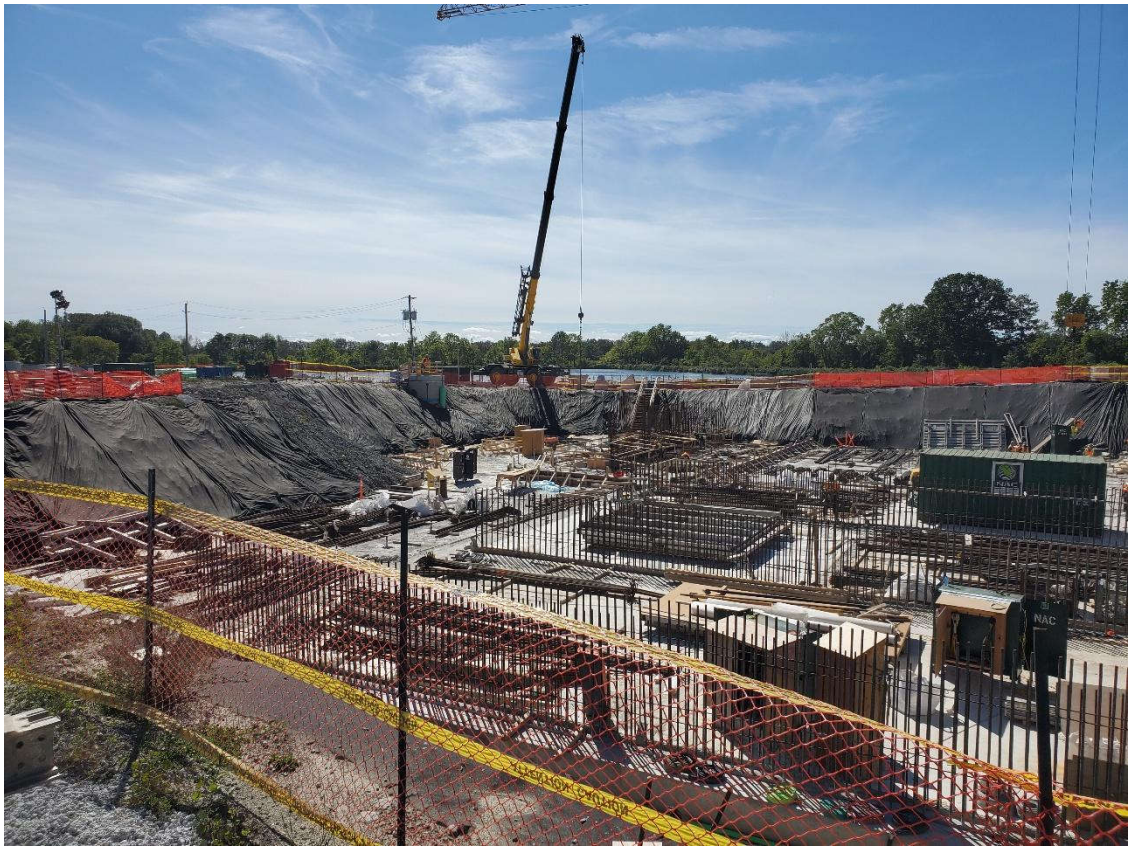


Photo 10: September 22 (aeration and clarifier tanks)

PROGRESS UPDATE REPORT NO. 9 - PHOTOS



Photo 11: September 22 (tank wall rebar)



Photo 12: September 23 (hopper rebar)

PROGRESS UPDATE REPORT NO. 9 - PHOTOS



Photo 13: September 24 (headworks building)

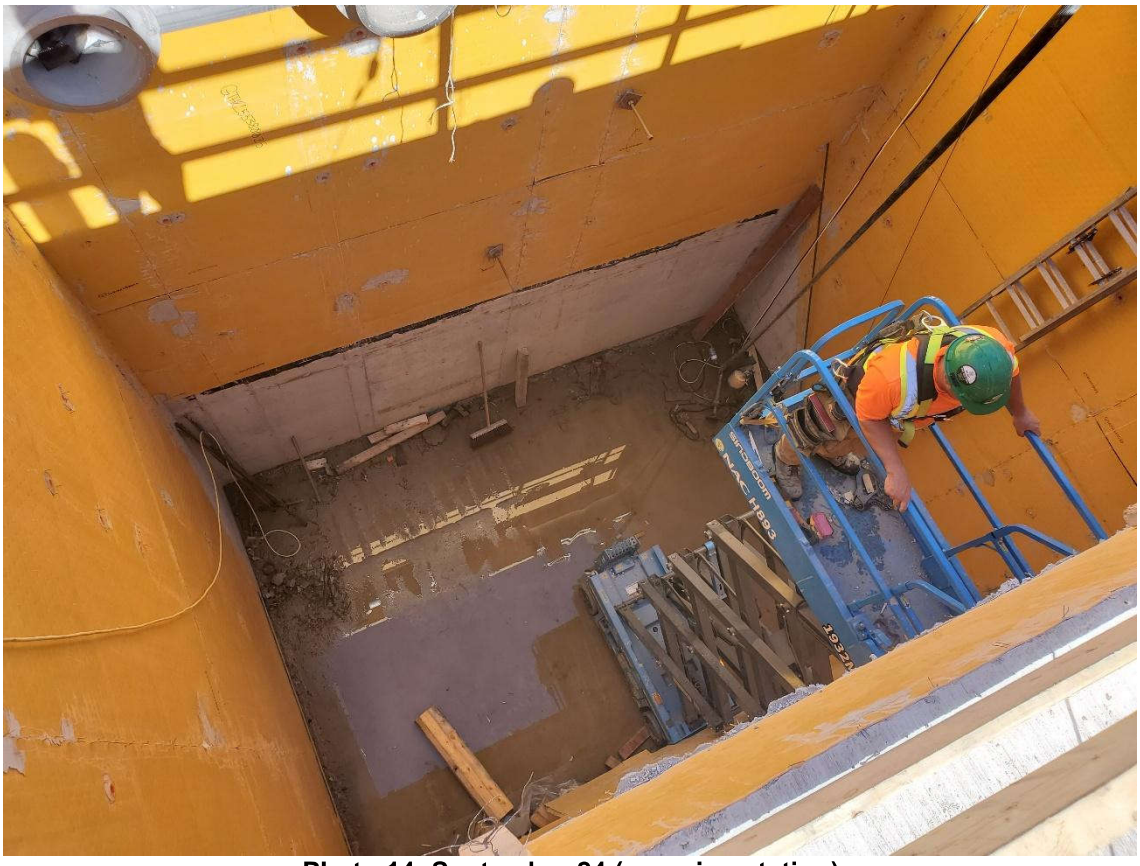


Photo 14: September 24 (pumping station)

PROGRESS UPDATE REPORT NO. 9 - PHOTOS



Photo 15: September 24 (admin building)



Photo 16: September 25 (Municipal Pit)

PROGRESS UPDATE REPORT NO. 9 - PHOTOS



Photo 17: September 30 (pipe installation)



Photo 18: September 30 (clarifier tanks)

PROGRESS UPDATE REPORT NO. 9 - PHOTOS



Photo 19: September 30 (admin building)
